# UNCLASSIFIED AD 429790

# DEFENSE DOCUMENTATION CENTER

**FOR** 


SCIENTIFIC AND TECHNICAL INFORMATION

CAMERON STATION, ALEXANDRIA, VIRGINIA



UNCLASSIFIED

NOTICE: When government or other drawings, specifications or other data are used for any purpose other than in connection with a definitely related government procurement operation, the U. S. Government thereby incurs no responsibility, nor any obligation whatsoever; and the fact that the Government may have formulated, furnished, or in any way supplied the said drawings, specifications, or other data is not to be regarded by implication or otherwise as in any manner licensing the holder or any other person or corporation, or conveying any rights or permission to manufacture, use or sell any patented invention that may in any way be related thereto.



00400

C-BAND TRIODE-CAVITY OSCILLATORS
PRODUCTION ENGINEERING MEASURE

SECON.) QUARTERLY PROGRESS REFORT

31 AUGUST 1963 THROUGH 30 NOVEMBE: 1963

CONTRACT NO. DA 36-039-AMC-01474(E)

ORDER NO. 21049-PP-63-81-81

U. S. ARMY ELECTRONICS MATERIEL AGENCY
PHILADELPHIA, FERRSYLVANIA

FEB 1 0 1964

CLASSIFICATION - NONE

RECEIVING TUBE DEPARTMENT

GENERAL ELECTRIC
OWENSBORO, KENTUCKY

#### C-BAND TRIODE-CAVITY OSCILLATORS, PRODUCTION ENGINEERING MEASURE

#### SECOND QUARTERITY PROGRESS REPORT

## 31 AUGUST 1962 THROUGH 30 NOVEMBER 1963

- Objective: (1) To optimize performance of the triode-cavity combination.
  - (2) To improve manufacturing methods.
  - (3) To assure more uniformity of product.
  - (4) To minimize the physical size of the cavity.
  - (5) To demonstrate 5 units per day production capability.
  - (6) To prepare and distribute progress reports.
  - (7) To prepare the Step II Report covering a rate of 1,000 units per month.

CONTRACT NO. DA 36-039-AMC-01474(E)

ORDER NO. 21049-PP-63-81-81

SIGNAL CORPS INDUSTRIAL PREPAREDNESS PROCUREMENT REQUIREMENTS NO. 15

CLASSIFICATION - NONE

REPORT BY . J. D. MARSHALL

#### TABLE OF CONTENTS

	Title	Page					
1.0	ABSTRACT	1					
2.0	TURPOSE	2					
3.0	MARRATIVE AND DATA						
	3.1 TEST EQUIPMENT	3					
	3.2 CW OSCILLATOR	4					
	3.3 Y-1251 CERAMIC TRIODE FOR CW OSCILLATOR	10					
	3.4 PULSE OSCILLATOR						
	3.5 Y-1252 CERAMIC TRIODE FOR PULSE OSCILLATOR	17					
4.0	CONCLUSIONS	18					
5.0	PROGRAM FOR THE NEXT INTERVAL	19					
	5.1 PROGRESS CHART	20					
6.0	PUBLICATIONS, REPORTS AND COMFERENCES	24					

#### 1.0 ABSTRACT

Pulse and CW cavity oscillators were a scholed for the first engineeric sample. Representative life tests have been completed. Operating characteristics of cavities are summarized. Modifications in triode design are being studied.

#### 2.0 PURPOSE

The objectives of this contract are to optimize performance as defined of specifications SCL-7001/82 and SCL-7001/83, to improve manufacturing methods, to assure more uniformity of product, to minimize the physical size of the cavity, to establish a capability to produce at the rate of 5 units per day each of oscillator types EL-PO(X-1) and EL-LO(X-1), and to prepare a Step II Report covering a production rate of 1,000 units per month.

The triode electron tube is the heart of the end device. It has root been established that, to a great extent, tube design intimately affects optom design of the cavity. Therefore tube design refinements are expected to improve product uniformity while maintaining optimum performance in a cavity of the smallest practical size. Data on tube performance and cavity performance must be taken and evaluated. A tube test specification must be established which will more accurately predict operation in a cavity oscillator.

By evaluation under various conditions, it is intended to reflect the benefits of this work in optimized cavity performance, and that such performance is assured during the expected life of the device. This evaluation includes tests for effects of shock, fatigue, vibration, load variation, supply voltage variation, ambient temperature cycling, and life tests.

Test requirements for triode and cavity oscillators, types EL-PO(X-1) and EL-IO(X-1). are defined by SCL-7001/82 and SCL-7001/83, dated 16 October 1962 and 23 October 1962 respectively, as amended.

#### 3.0 KARRATIVE AND DATA

The program during this period has consisted of:

- 1. Preparation of test equipment.
- Fabrication of triodes and of cavity parts for the first engineering sample.
- 3. Assembly and testing CW and pulse cavity oscillators.
- 4. Investigation of design refinements in both triodes.

#### 3.1 TEST EQUIPMENT

The life test equipment for both the CW and pulse cavit s has been completed. The units consist of 10 positions for each type.

Work on the pulse driver adaptor to be used with the universal pulse test set has been stopped as a universal driver unit is being constructed for this set which will be satisfactory for testing the EL-FN(X-1) cavities as well as the Y-1252 tubes prior to assembling in the cavities. This equipment will be completed in time for the preproduction run.

A tube test cavity for the Y-1252 pulse tube has been evaluated and found satisfactory for tube testing.

Design work has started on a tube test cavity for the Y-1251 CW tube. This cavity will be used in a universal CW RF power output test set which is part of the general laboratory test equipment.

The temperature cycling test chamber is being checked out with a five position adaptor panel which was designed and constructed for both the CW and pulse cavities. It was found feasible to use

the existing laboratory chamber. A modulator unit similar to the one used for the pulse life test will be modified to permit temperature tests to be run on five cavities simultaneously. DC power sumplies are available for the CW cavity tests.

A test and essembly area has been assigned exclusively to this contract. This will allow a closely supervised operation and will help o make most efficient use of the precision measuring equipment available. More accura a measurement of performance on life continuation in made than if the frequency measuring equipment were a cotely located and transfer instruments had to be used.

# 3.2 CW OSCILLATUR, EL-LO(X-1)

Eighteen cavities were assembled using a 5/8" diameter body similar to that used for the pulse cavity. This design permits standardization of several . the cavity parts for both the CW and pulse cavities.

Tables I, II, IV and V summarize the performance of these cavities. The following design objectives are included in the program for the next sample:

- 1. Improve the performance at the high frequency end of the band.
- 2. Achieve more uniform output across the band.
- 3. Reduce the plate current to less than 20 mA maximum.
- 4. Reduce frequency pulling with load changes.

It is probable that these design goals can be met by further adjustment of cavity impedances, selection of grid cylinders to

TYPE EL-LO(X-1) C-BAND CW TRIODE and CAVITY OSCILLATOR

# Operating Characteristics - First Engineering Sample

	5250 Mc		560	0 Mc	6050 Mc
SN	Po	功	Po	<u>IS</u>	Po Ib
236	175	18.1	98	16.8	11 24.5
237	75	17.0	69	16.1	5 25.0
238	12	23.6	18	22.6	F - Max = 5800 Mc
239	29	15.3	32	14.9	F - Max = 5875 Mc
240	155	25.2	202	22.2	14 22.3
241	88	18.5	112	18.0	15 20.2
242	75	15.6	92	15.0	8 19.0
243	175	22.0	134	19.5	10 24.3
21414	65	16.1	56	16.0	7 25.0
245	139	23.6	130	20.0	34 24.5
246	٥6	22.3	198	19.8	58 21.8
247	61	14.7	65	14.2	5 21.0
248	68	15.0	60	14.5	4 23.7
249	119	16.8	108	16.2	19 19.8
250	116	17.8	86	17.0	14 24.3
251	36	24.0	79	21.6	15 25-4
252	53	17.8	100	17.0	7 20.2
253	125	19.3	71	19.0	3 29.5

#### Objective Specifications

Power output = 5 Mw min Frequency Range = 5250 - 6050 Mc Ib = 20 mAdc max

Ef = 6.3 Vac £bb- 150 Vdc

TABLE II

# TYPE EL-LO(XO1) C-BAND CW TRIODE end CAVITY OSCILLATOR

# Operating Characteristics - First Engineering Sample

# Load Variation

•••	_	F = 5	400 Mc	F = 5900 Mc					
SN	<u> AF -</u>	Mc/S	△Po	-db	AF -	Nc/S	△Po	-db	
570	-1.0	+1.0	<b>40.</b> 5	-0.75	-1.6	+3.4	+1.2	ر ـ	
241	-2.0	<b>40.</b> 8	+0.4	-0.6	-4.2	+5.9	+1.5		
575	-3.2	+1.5	+0.4	-0.5	-4.6	+6.6	+1.8	-0.75	
249	-4.0	+1.4	<b>40.3</b>	-1.25	-6.è	+8.2	+1.4	-1.1	
251	-4.8	+1.4	+0.4	-1.6	-6.6	+8.0	+1.6	-1.3	

# Objective Specifications

 $\Delta F = \pm 3 \text{ Nc/S}$  $\Delta Po = \pm 2 \text{ db}$ 

Ef = 6.3 Volts Ebb = 150 Vdc VSWR= 1.5 ± 0.1

TABLE III

# TYPE EL-LO(X-1) C-BAND CW TRIODE and CAVITY OSCILLATOR

## Operating Characteristics - First Engineering Sample

## Supply Voltage Variation

	F = 5250  Mc						F = 5950  Mc				
SN	<u> </u>	vc/S	AP0	<b>-</b> ₫Ъ		<u> △F - I</u>	ic/S	ΔPo	-ძა		
240	+0.13	-1.26	-0.75	<b>*1.25</b>		<b>+0.75</b>	-2.01	-1.75	+1.5		
241	-0.16	+0.45	-1.2	+1.1		-2.32	+2.35	-1.9	÷3.6		
242	-1.52	+1.67	-1.6	+1.55		-3.06	+3.34	-2.4	+2.2		
243	+0.68	-1.55	-1.55	+1.25		-0.72	+0.56	-2.25	+ ;		
249	-1.38	+1.32	-1.65	+1.45		-3.12	+3.24	-2.25	+1、ブ		

## Objective Specifications

 $\Delta F = \frac{4}{2} \frac{4}{3} \frac{\text{Mc/S}}{\text{db}}$  $\Delta Po = \frac{4}{2} \frac{3}{3} \frac{\text{db}}{\text{db}}$ 

Ef = 6.0 - 6.6 VacEbb = 1/12 - 155 Vdc

TABLE IV

# TYPE EL-LO (X-1) C-BAND CW TRIODE and CAVITY OSCILLATOR

# Operating Characteristics - First Engineering Sample

## Vibration

SN	#Freq - Mc/S	Po - mW	$\frac{\text{Pos. X1}}{\triangle F - \text{Mc/S}}$	Pos X2  F - Mc/S	Pos. Y1  AF - Nc/S
237	5950.0	9.5	0.1	0.2	0.4
2140	5950.0	13.0	0.2	0.5	0.4
243	5950.0	8.1	0.1	0.2	1.C
21,4	5950.0	7.7	0.1	0.2	0.3

\* Test run at 5950 Mc instead of 5900 Mc to make it compatable with fatigue.

Objective Specification:  $\Delta F = 4 2 \text{ Mc/S max}$ .

1	8	t	ſ	g	u	e

SN	Freq - Mc/S	Po - mW	AF - Mc/S	ΔP0 - %
237	5950.0	9.5	-0.5	<b>-1</b>
240	5950.0	13.0	-0.5	+23
243	5950.0	8.1	-1.0	+ 2
244	5950.0	7.7	0	- 3

Objective Specification:  $\triangle F = 4 \text{ Mc/S}; \triangle Po = \pm 30\%.$ 

# Shock

SN	Freq - Mc/S	Pc - mW	AF - Mc/S	△ Po - %
245	5950.00	46.0	+3.25	0
247	5950.00	10.6	-2.00	0
248	5950.00	8.0	0	0
251	5950.00	22.0	+1.62	+9.1

Objective Specifications:  $\triangle F = \pm 4 \text{ Mc/S}$ ;  $\triangle Po = \pm 30\%$ 

TABLE V

TYPE EL-LO(X-1) C-BAND CW TRIODE
and CAVITY OSCILLATOR

# Operating Characteristics - First Engineering Sample

L	11	e	T	e	S	t

SN	Hours Life	F - Mc/S	Po - mW	Ib - mA	AF - Mc/S	2.Po - %
236	0 94 208 334 429 501	5249 5251 5251 5251 5251 5250	262 269 269 264 258 252	19.4 19.9 19.9 19.6 19.5 19.2	+2 +2 +2 +2 +2 +1	+2.7 +2.7 +0.8 -1.5 -3.8
250	0 94 208 334 429 501	5240 5241 5241 5239 5241 5239	148 154 154 154 154 148	19.4 19.7 19.7 19.7 19.6 19.4	+1 +1 +1 +1 -1	+4.1 +1.1 +4.1 +4.1
. 246	0 94 208 334 429 501	5942 5942 5942 5942 5942	94 95 98 110 110	21.8 22.0 22.0 21.9 21.7 21.5	0 0 0 0 0	+1.1 +4.3 +17.0 +17.0 +13.8
252	0 94 208 334 429 501	5937 5939 5940 5940 5940 <b>5938</b>	19 20 21 23 25 26	19.5 19.5 29.5 20.0 20.5 20.5	+2 +3 +3 +3 +1	+5.3 +10.5 +21.0 +31.6 +36.8

Objective Specifications:  $\triangle F = \pm 8 \text{ Mc/S}$ ;  $\triangle Po = \pm 70\%$ ; Po = 1.0 mW min. Ef = 6.3 volts, Ebb = 150 volts, T = 500 Hours. provide optimum feedback for specific tubes, and careful adjustment of the output coupling.

Frequency stability over the required ambient temperauture range has not been fully evaluated due to the equipment limitations. Preliminary tests indicate that the requirements called for in specifications SCL-7001/83 can be met.

The first engineering samples to be furnished during the next period have been tested preparatory to submission. Shock, fatigue and life tests have been successfully completed. This infon wion is included in Tables TV and V.

#### 3.3 CW TRIODE, Y-1251

CAL TONIES CONTRACTOR OF THE PARTY OF THE PA

Tubes were fabricated with a slightly larger external anode diameter to permit the use of standard tooling during machining of cavity parts. Orders for screw machine anodes will not be placed until dimensional requirements of the cavity have been established.

Tubes were fabricated with the larger anode aismeter for an internal evaluation of the cavity design and for the second engineering sample. Tusting and evaluation has been started.

Tube design improvements, which were reported in the 7486 PEM Contract No. DA 36-039-SC-86738, have been successfully applied to the Y-1251. The new cathode spray masks were used during cathode coating to prevent loose particles of coating material. Hecters were used which had the surface of the heater coating darkened with tungsten. Tests on these tubes are still in progress.

#### 3.1: PULSE OSCILLATOR, EL-PO(X-1)

Tables VI, VIII, VIII, IX and X show the operating characteristics achieved with eighteen first engineering sample cavities.

The areas where additional engineering effort is required are:

- Develop techniques for pre-selecting grid resistors before assembly.
- Improve the performance at the high frequency end of the band.
- 3. Reduce the frequency pulling with load variation.

Some progress has been made in establishing a correlation between the grid resistor required for 600 mA peak plate current in the tube test cavity and the value of grid resistor required in the type EL-PO(X-1) cavity for the same current. As more data from additional tubes and cavities are accumulated, this factor should resolve itself.

The power output response across the band and the frequency pulling can be optimized by careful adjustment of the output coupling and, where necessary, selection of grid cylinder lengths to match tube characteristics.

As in the CW cavities, temperature testing has not been completed due to equipment limitations, but preliminary data indicates that the requirements in SCL-7001/82 can be met.

The first engineering samples to be furnished during the next period have been tested preparatory to submission. Shock, fatigue and life tests have been successfully completed. This information

TABLE VI

# TYPE PL-PO(X-1) C-BAND PULSED TRIODE BELL CAVITY OSCILLATOR

# Operating Characteristics - First Engineering Sample

	Peak !	ower O equenc				Peak P Freq		urrent - Mc/S		
<u>sn</u>	<u>5350</u>	51100	<u>5650</u>	5900	<u>5950</u>	<u>5350</u>	5400	<u>5650</u>	<u>5900</u>	<u>5950</u>
100 101 102 103 104 105 106 107 108 109 110 111 112 113 114 115	72 180 61 58 137 100 60 72 28 137 155 128 202 42 55	80 190 62 62 137 105 82 35 111 150 122 140 200 48	70 125 55 64 127 67 55 67 50 110 80 127 140 58	55 88 36 42 86 36 35 35 42 77 58 85 81 46 38	43 77 32 37 74 30 28 30 29 34 72 48 72 65 41 26	560 640 430 450 600 800 590 640 700 750 640 450	650 680 850 630 630 700 720 640	530 600 460 640 510 700 560 550 640 630	500 570 390 420 550 540 550 630 590 590 570 420	490 570 380 510 510 570 490 650 490 580 590 410
116 117	78 100	7 <i>5</i> 98	60 62	47 38	38 32	630 640	610	560 550	510 460	500 450

# Objective Specifications

Peak Power = 30 watts min. Freq. Range = 5350 - 5950 Mc Peak Current = 600 mA max.

Ef = 6.3 Vac

eb = 1000 V pk.

prf= 4000 pps

tp = 0.5 usec.

TABLE VII

## TYPE EL-PO(X-1) C-BAND PULSED TRIODE and CAVITY OSCILLATOR

# Operating Characteristics - First Engineering Sample

# Load Variation

		F - 54	00 Mc			F = 59	OO Mc	
SN	<u> </u>	`tc/S	<b>▲</b> po	<u>-এচ</u>	ΔF	Mc/S	<u> </u>	-db
100	-3.6	+3.2	+0.4	-0.6	-1.2	+1.4	+0.7	-0.85
101	-2.1	+2.0	+0.2	-0.5	-0.3	+0.2	+1.05	-1.2
102	-4.5	+5.5	+0.75	-1.05	-1.7	+1.5	+1.0	-1.0
103	-4.9	+5.9	+0.6	-1.3	-1.4	+1.2	+2.0	-0.75
104	-4.2	+6.5	+0.5	-1.0	-1.4	+1.7	+0.6	-0.95
105	-3.2	+1.6	+1.1	-0.7	-0.3	+0.6	+1.35	-1.4
106	-4.5	+4:.4	+0.9	-1.2	-1.0	+0.8	+0.75	-1.05
107	-2.9	+1.9	+0.7	-1.0	-0.6	+0.2	+1.1	-1.3
108	-2.6	+2.8	+0.9	-0.35	-1.0	+0.3	+1.35	-1.55
109	-5.6	+3.7	+1.3	-0.65	-0.9	+1.2	+1.3	-1.45
110	-2.6	£2.7	+0.4	-0.45	-1.6	+1.0	+0.7	-0.75
111	-2.8	42.8	<b>*0.3</b>	-0.6	-1.0	+1.0	+0.35	-1.1
112	-2.0	<b>*</b> 3.6	+0.2	-0.6	-0.8	+1.6	+0.35	-1.4
113	<b>-2.</b> 0	<b>43.6</b>	<b>40.5</b>	-0.5	-1.1	+1.8	+0.75	-1.2
114	-3.4	<b>+3.0</b>	<b>40.9</b>	-1.6	-1.0	+0.6	+0.7	-0.35
115	-2.7	+3.6	<b>₩</b> 0.35	-0.65	-1.0	+2.0	+0.5	-1.25
116	-2.5	42.L	<b>41.0</b>	-0.75	-1.2	+0.6	+0.9	-1.25
117	-1.8	♦2.9	+0.3	-0.6	-0.8	+0.6	+0.95	-1.15

# Objective Specifications

AF = ± 3 Mc Apo = ± 2 db VSWR = 1.5 ± 0.1

Ef = 6.3 Vac eb = 1000 V pk. prf = 4000 pps

tp = 0.5 usec.

#### TABLE VIII

# TYPE EL-PO(X-1) C-BAND PULSED TRIODE and CAVITY OSCILLATOR

# Openiting Characteristics - First Engineering Sample

# Supply Voltage Variation

	F = 540	00 Mc	F = 5900 Mc	
SN	△ F Mc/S	△po -db	<u> </u>	> -db
100	-0.15 +0.9	<b>-3.1 +1.9</b>	-0.26 +0.67 -3.0	D5 +2.7
101	-4.0 +4.0	-2.5 +0.7	-5.0 +4.0 -1.5	55 +0.6
i11	-3.3 +4.38	-1.35 +0.2	-1.67 +1.93 -1.6	55 +0.45
116	-2.55 +3.09	-1.3 +0.45	-1.16 +0.79 -1.7	7 +0.75
117	-4.68 45.4	-2.4 +0.5	-1.73 +0.85 -2.5	55 +1.2

# Objective Specifications

$$\Delta F = \frac{+}{2} \frac{8 \text{ Mc/s}}{3 \text{ db}}$$

Ef = 6.0 - 6.6 Vac eb = 950 - 1050 V pk. prf = 4000 pps tp = 0.5 usec.

TABLE IX

# TYPE EL-PO(X-1) C-BAND PULSE TRIODE and CAVITY OSCILLATOR

# Operating Characteristics - First Engineering Sample

## Vibration

SN	Freq - Mc/S	po - Watts	Pos. XI  AF - Mc/S	Pos. X2  AF - Mc/S	Pcs. Y.
100	5900	42	< 0.1	< 0.1	< 0.1
104	5900	85	< 0.1	`0.2	0.1
105	5960	30	< 0.1	< 0.1	< 0.1
106	5900	33	0.3	0.4	0.3

Objective Specification:  $\triangle F = + 3.0 \text{ Mc/S Max}$ .

### Fatigue

SN	Freq - Mc/S	po - Watts	AF - Mc/S	<u> Дро - %</u>
100 104 105 106	5900 5900 5900 5900	42 85 30 33	NOTE	

NOTE: No detectable change in frequency or power output was seen.

Objective Specifications:  $\Delta F = \pm 8 \text{ Mc/S}$ ;  $\Delta po = \pm 20\%$ .

# Shock

SN	Freq - Mc/S	po - Watts	AF - Mc/S	<u> Дро - %</u>
107	5900.00	46	-1.50	+15.2
108	5900.00	39	-1.79	-7.7
114	5900.00	717	-2.43	+18.2
115	5900.00	80	-0.13	-6.3

Objective Specification:  $\Delta F = \frac{1}{2} 8 \text{ Mc/S}$ ;  $\Delta po = \frac{1}{2} 20\%$ 

TABLE X TYPE FL-PO(X-1) C- BAND PULSE TRIODE and CAVITY OSCILLATOR

# Operating Characteristics - First Engineering Sample

L	ife	Te	st

SN	Hours Life	F-Mc/S	po-Watts	<u>ip-mA</u>	AF-Mc/S	APU-#
102	0 25 50 75 100	5391 5393 5392 5388 5387	91 67 77 63 57	440 400 400 360 360	 +2 +1 -3 -4	-26 -15 -31 -37
103	0 25 50 75 100	5396 5395 5396 5390 5389	91 79 98 86 84	450 420 460 440 440	 -1 0 -6 -7	 -13 + 8 - 5 - 8
112	0 25 50 75 100	5894 5899 5898 5892 5895	99 91 101 91 90	600 590 600 560 560	+5 +4 =2 +1	- 8 + 2 - 8 - 9
113	0 25 50 75 100	5900 5900 5900 58911 58514	104 104 112 97 83	620 620 640 600 590	0 0 -6 -6	0 • 8 - 7 -20

## Objective Specifications

AF = 4 8.0 Mc/S Max Apo = 7 50% Max po = 20 Watts Min T = 100 Hours

Ef = 0.3 volts

eb = 1000 volts, tp = 1.0+0.5 usec Prf = 2000 pps, approx. F = 5900 and 5400 Mc

is included in Tables IX and X.

#### 3.5 Y-1252 CERAMIC TRIODE FOR PULSE OSCILLATOR

Tube design improvements already discussed (3.3 - page 10) were also applied in the ceramic triode for pulse operation. A spray mask similar to that used for the .100" diameter cathode of the Y-1251 has been used during the coating operation on the .120" diameter cathodes of the Y-1252.

Testing and evaluation of tubes fabricated for the second engineering sample is now complete. Initial assembly of thes tube-cavity oscillators will be done during the next period.

Aging and stabilizing schedules are being studied to establish tube processing which will eliminate or reduce oscillator re-adjustment due to changing tube parameters during early life. The present technique is to allow for a run-in period in the oscillator, followed by re-adjustment or substitution of the grid resistor.

#### 4.0 CCACLUSIONS

The first engineering sample is being prepared for submission. Shock, fatigue, and life tests have been successfully completed. Effort will be made to improve performance at the high frequency end of the band and to reduce frequency pulling with load variation. Satisfactory inclusion of darkened heaters and the use of improved spray masks has been done for ceramic triodes for both CW and pulse operation.

#### 5.0 PROGELIM FOR THE MEXT INTERVAL

Work will continue toward optimizing cavity dimensions and establishing assembly techniques. Data will be accumulated to permit pre-selection of grid resistors and cylinder lengths to match individual tube characteristics. The temperature test chamber and associated equipment will be completed and tests will be run on cavities from the first engineering sample. Life testing of the CW cavities from the first engineering sample will continue to failure or until the positions are required for current production units.

Aging and stabilizing schedules will be established for both Y-125 and Y-1252. Life tests for evaluating effects on tube characteristics and oscillator performance will be started.

5.1 - PROGRESS CHART - C-BAND TRIODE-CAVIT OSCILL& TORS DA-36-039-ANC-OIL74(E)

1963

Test Equipment

TASK I - DESIGN

# <del>                                    </del>	-	<u>.                                     </u>	1	9			•		4	4	-	7	•	2	2	-	
<b>8</b>		-	-	-	_	_	١	ł	ļ	١		İ	١		ľ	I	
life test - Pulse & CV	<b>88</b>		8g 0000	OHAR OHAR	(SE)		<u> </u>										
it adaptors dipment clent test facilities of in-plant test					<u> </u>	4H^	ZHM.	4 H H H H H H H H H H H H H H H H H H H	8						······································		
nlant test facilities unt test facilities									<u>`</u>	&	Ŕ						 
(temporary)													+				 
x 31g sippose	98		6														
rbin welding 11g	<u> </u>	3 9															 
thine saodes		нн	98 98		H	X X	72						<del>,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,</del>				
	н	නු <del>x</del>	H 워H	H		X X IS	<b>1</b> 0										 

1. Procure spectrum analyse 2. Construction - pulse Po 3. Portable test set - CW 8 h. Adaptors - CW Po test set 5. Adaptors - Pulse Po test 6. 10 positions CW life test 7. 10 positions Pulse life 8. Tube test cavities - Pul 9. Procure test socket adaptor in Temperature coefficient ll. Temperature coefficient ll. Request inspection of infactilities like inspection of infactilities ll. Approval of in-plant in Approval of in-plant in Approval of in-plant in the manufacture mathematics.

B. Improved Hamifacturing Hethods
1. Anote turning jig (temporary
a. Design
b. Procure
2. Anode solder shin welding jil
a. Design
b. Procure
3. Heater pin solder rhim weldt

b. Procure
i. Procure screw machine sacdes
5. Heater insulator - sublimation sh
a. Design
b. Procure


Design

Notes

I - Anticipated Progress
 ) - Actual Progress
 ) - Completion
 Numerical representations indicate terminal dates

-20-

5.1 - PROCRESS CHART - C-BAND TRIODE-CAPITY OSCILLATORS DA-36-039-ARC-01474(B)

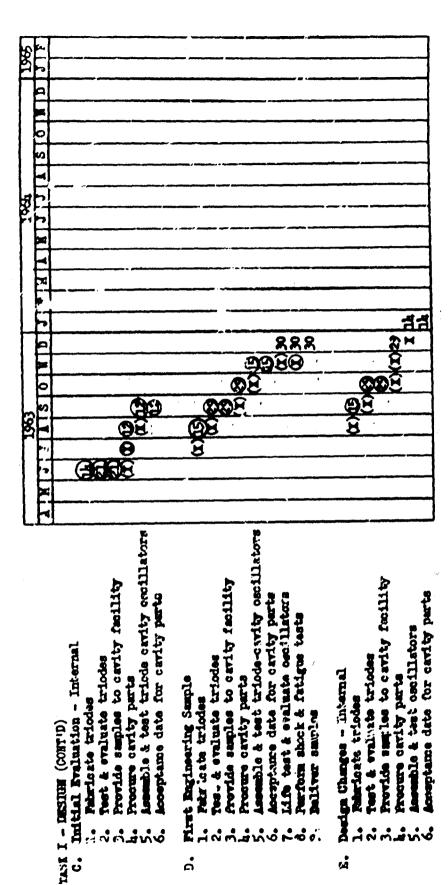

x - inticipated Progress
 x - interpreted Progress
 x - interpreted Progress
 x - completion
 x - completion
 x - inticipate terrainal dates

21.

.1 - PROGRESS CHART - C-BAND TRIODE-CAVITY OSCILLATORS DA-36-039-ANC-01474(B)

5	۵.				
1	-				
	Δ				
	æ				
	0				
- (	S				8
	¥				
3					222
1	2			<u> </u>	Энн
	E		9	HH	нн
	=	23	\$\$	<b>₹</b> ₩	
	E	N 8 8 H H	ਸ਼ਮ	н	
	ø.	%н нн	н	H	
	2	4 % % % % % % % % % % % % % % % % % % %			
	2	NAT.			
	=	880			
	0				
ン	2			······	
2027					
	1				
	2				
	~				
_	上				
		P. Second Engineering Sample 1. Fahr-faste triodes 2. Test & evaluate triodes 3. Test & evaluate triodes 4. Provide samples to cavity facility 5. Procure cavity purts 6. Assumble & test oscillators 7. Acceptance date for cavity purts 8. Idfo test & evaluate oscillators 9. Perform shock & fatigue tests 10. Deliver samples	H		Acceptance date for cartify parts Life test & evaluate oscillators Furform shock & fatigue tests Deliver samples Acceptance date for pro-production run samples
		TASK T	18. W	ะรู้เก๋ง	<b>-8</b> % % ¼

Notes:

X - Antinipated Progress
() - Actual Progress
() - Completion
() completion
() merrical representations indicate terminal dates

5.1 - PROGRESS CHART - C-BAND TRIODE-CAVITY OSCILLATOR DA-36-039-ANC-01474(E)

治	-			·		22	8
	;	يب د سرور و سالی و د سال	0.0	3888			
-							
F	4		H	нн	&		
٩	┿		H	нн	<del></del>		_
0	1	- 88 H					
	1	সন			8		
30	2	Fig.		~	•	\$	
aF	<u> </u>						
2	5				23		
•	4						
5							
5.	4				23		
F	키						
-	寸						
-	計				\$3		
k	5						
k	7						
83	4	<del></del>			⊗		
7	,†				0		
	;†				200	වුණු	
,							
l E	#						-
					. <b>ដ</b>	90	

Provide samples to cavity facility

rocure cavity parts

That & evaluate triodes

TACK III - PRODUCTION RUN Pabricate triodes Assemble & test oscillators
Acceptance date for cavity parts
Life test & evaluate oscillators

Perform shock & fatigue tests Deliver samples

IV - REFORTS

TASK

Quarterly Intent to use proprietary information making triodes That reports on pre-production samples Nata requirements control plan Inspection & quality control plan Hilestone or progress chart Bills of material General report v. & ~ & &

Pinel report

I - Antidipated Progress
 ) - Actual Progress
 ) - Completion
 ) - Completion
 ) - Completions

# 6.0 PUBLICATIONS, REPORTS AND COMPERENCES

- 6.1 PUBLICATIONS None
- 6.2 REPORTS First Quarterly Progress Report
  29 April 1963 through 30 August 1963

#### 6.3 CONVERENCES

1. Organizations and personnel present:

#### UBAEMA

L. Coblentz

General Electric Co.

J. D. Campbell

L. F. Jeffrey

J. D. Marshall

H. L. Thorson

Place and Date: General Electric Co. Owensboro, Kentucky

15 October 1963

### Subject:

Review of progress to date and to discuss future schedule.

2. Organizations and personnel present:

TRAK Microwave Corp. B. F. Gregory

General Electric Co. L. F. Jeffrey

Place and Date:

TRAK Microwave Corp. Tampa, Florida

October 7 and 8, 1963

#### Subject:

To discuss cavity parts being supplied to G.E. under sub-contract and to witness inspection and testing of these parts.

# GENERAL ELECTRIC COMPANY ELECTRONIC COMPONENTS DIVISION TURE DEPARTMENT OWENSBORO, KENTICKY

Subject: Second (2nd) Quarterly Report
Order No. 21049-PP-63-81-81
Contract No. DA-36-039-AMC-01474(E)

Philadelphia, Pa. 19103

U. S. Army Electronic Materiel Agency

Philadelphia 3, Pennsylvania

Advisory Group on Electronic Devices 346 Broadway, 8th Floor ATTN: Chairman, Low Power Devices New York 13, New York 10013	Number of Copies
Defense Documentation Center (TISTA-1) Cameron Station Alexandria, Virginia	10
Commanding Officer U. S. Army Electronics Research & Development Laboratory ATTN: SELRA/SL-PRM, Mr. Sheppard Fort Monmouth, New Jersey 07703	1
Commanding General U. S. Army Electrooics Command ATTN: AMSEL-PP (PD-5b) Fort Monmouth, New Jersey 07703	2
Commanding Officer U. S. Army Electronics Materiel Support Agency ATTN: SELMS-PFE, Mr. E. Anderson Fort Monmouth, New Jersey 07703	2
Canadian Liaison Officer Army Materiel Command Tempo 7, Room 1067 Washington, D. C. 20315	1
Bell Telephone Laboratories Murray Hill, New Jersey ATTN: Librarian	1
Commanding General U. S. Army Electronics Materiel Agency 225 South 18th Street ATTN: SELMA-R2b, Mr. L. Coblentz	Balance of Copies
